

KENDRIYA VIDYALAYA SANGATHAN (WORKS DIVISION)

STATUS OF ON GOING
CONSTRUCTION WORK OF SCHOOL
BUILDING PROJECTS

AS ON
01.06.2018




Status of Ongoing Construction work of School Building Projects as on 01.06.2018(State Wise)

Sl. No.	Name of Kendriya Vidyalaya	AA & ES (Rs. in lakh)	Date of Sanction	Construction Agency	Date of Start	Physical Progress upto date	Stipulated date of completion	Amount released till date (Rs. in lakh)	Remark
1	2	3	4	5	6	7	8	9	11

(A) SCHOOL BUILDING UNDER CONSTRUCTION

Andhra Pradesh

1	Tenali (A-I type+09 SQ+BW)	1600.94	05.10.2015	HSCL	17.02.16	76%	16.08.17	1420.00	180.94	Work in Progress TDC- 31.06.2018
---	-------------------------------	---------	------------	------	----------	-----	----------	---------	--------	--

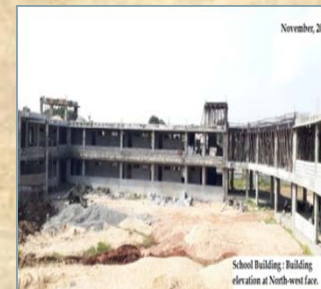

Arunachal Pradesh

2	Miao (A-I type +09 SQ+BW)	2383.70	13.01.2015	AP PWD	01.08.15	40%	28.02.18	1700.00	683.70	Slow Progress due to N.E. Region problem.
---	------------------------------	---------	------------	--------	----------	-----	----------	---------	--------	---



3	Tuting (A-I type+09 SQ+BW)	2431.81	12.10.2015	AP PWD	10.01.16	45%	March,2018	1320.00	1111.81	Slow Progress due to N.E. Region problem
---	----------------------------------	---------	------------	--------	----------	-----	------------	---------	---------	---



Assam


4	Rangiya (B-Type+SB + B/w)	2264.95	01.09.2016 03.05.2017	AP PWD	16.01.17.	50%	31.08.18	2020.00	244.95	Work in progress.
---	------------------------------	---------	--------------------------	--------	-----------	-----	----------	---------	--------	-------------------




5.	Haflong (A-Itype+09 SQ)	1751.23	15.12.2010	CPWD	13.08.13	96%	03.02.15	1750.00	1.23	Initial delay due to land dispute.
----	----------------------------	---------	------------	------	----------	-----	----------	---------	------	---------------------------------------



6.	Tamulpur (Atype+09 SQ+BW)	2196.62	12.09.2014 24.04.2015	CPWD	07.10.15	99%	06.04.17	2120.00	76.62	T.D.C-30.06.18 Slow progress due to shortage of fund.
----	------------------------------	---------	--------------------------	------	----------	-----	----------	---------	-------	--



7.	Golaghat (A-ltype+11 SQ+BW)	1885.41	08.05.2014	CPWD	27.04.15	91%	26.10.2016	1820.00	65.41	Delay/slow progress due to shortage of fund. TDC-30.06.2018
----	--------------------------------	---------	------------	------	----------	-----	------------	---------	-------	---

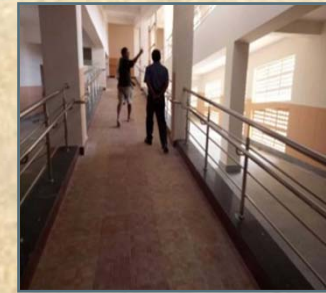

BIHAR

8.	Sasaram ('C'-Type+09 SQ + BW)	2584.79	07.12.2015 5.05.2016	HSCL	24.08.16	91%	23.02.18	2520.00	64.79	Work in Progress TDC-30.09.18
----	-------------------------------	---------	-------------------------	------	----------	-----	----------	---------	-------	-------------------------------



9.	Betia (A-Type+BW)	1301.66	24.06.2014	HSCL	25.07.14	88%	31.01.16	1120.00	181.66	Due to Bandh & Ban on sand. TDC-30.09.18
----	----------------------	---------	------------	------	----------	-----	----------	---------	--------	--



10.	Aniwan, Jehanabad B-Type+09 Sq+BW	2679.99	04.12.2014	CPWD	19.08.15	79%	18.02.17	1920.00	759.99	Initial delay due to land dispute. TDC-30.06.18
-----	--------------------------------------	---------	------------	------	----------	-----	----------	---------	--------	---



11.	Araria ('A'-Type+09 SQ + BW)	1535.45	25.03.2015	CPWD	02.04.16	80%	01.04.17	1420.00	115.45	Slow Progress by CPWD. TDC-30.06.18
-----	----------------------------------	---------	------------	------	----------	-----	----------	---------	--------	-------------------------------------



Chhatisgarh										
12.	Rajnandgaon('A'- Type+09 SQ+BW)	1625.93	24.08.2016	CPWD	17.12.16	85%	16.12.17	1320.00	305.93	Work in Progress. Shortage of funds.



13	Hasaud ('A'-Type+09 SQ+BW)	1597.03	01.09.16	CPWD	24.11.16	75%	23.11.17	1220.00	Work in Progress.TDC-30.06.18
----	----------------------------	---------	----------	------	----------	-----	----------	---------	-------------------------------



14	No 4 BCPP Korba ('A'-Type+09 SQ+BW)	1586.32	01.09.17	CPWD	24.11.16	75%	23.11.17	1220.00	366.32	Work in Progress.
----	-------------------------------------	---------	----------	------	----------	-----	----------	---------	--------	-------------------



15	Narayanpur ('A'-Type+09 SO+BW)	1694.01	20-06-2016 01.03.2017	BBJ&JCC	30.05.2017	21%	August 2018	420.00	1274.01	Delay on the part of construction agency in completing the formalities. Go ahead approval given on 01.03.2017
----	--------------------------------	---------	--------------------------	---------	------------	-----	-------------	--------	---------	---



DELHI

16	Sec.-28, Rohini @ ('B' Type)	1800.62	12.08.2014	AP PWD	08.12.17	30%	07.12.19	620.00	1180.62	Delay in approval of Drawings by MCD.
----	------------------------------	---------	------------	--------	----------	-----	----------	--------	---------	---------------------------------------



17	Sec-5, Narela B Type	2035.00	04.05.2007 07.08.2013	CPWD	21.05.15	96%	10.11.16	1420.00	615.00	TDC-30.04.18.
----	----------------------	---------	--------------------------	------	----------	-----	----------	---------	--------	---------------



Gujarat

18	Dahod ('A' Type + 09 SQ + BW)	1589.37	09.06.2015	CPWD	26.07.16	75%	25.10.17	820.00	769.37	Initial delay on the part of CPWD.
----	-------------------------------	---------	------------	------	----------	-----	----------	--------	--------	------------------------------------



19	Jetpur ('A-1' Type + 09 SQ + BW)	1252.79	27.05.2015	CPWD	22.07.16	75%	21.10.17	820.00	432.79	Initial delay on the part of CPWD. TDC-30.06.2018
----	----------------------------------	---------	------------	------	----------	-----	----------	--------	--------	---



20	Viramgaon (A-1, Type+BW)	1225.36	15.07.2014 08.10.2014	CPWD	21.09.15	80%	20.09.16	1020.00	205.36	Initial delay due to land problem.
----	-----------------------------	---------	--------------------------	------	----------	-----	----------	---------	--------	------------------------------------



Haryana

21	No.3 Faridabad ('B' Type SB+9SQ+BW)	2018.22	01.03.2017	DHPD	11.10.17	29%	10.10.19	820.00	1198.22	Recently Sanctioned.
----	-------------------------------------	---------	------------	------	----------	-----	----------	--------	---------	----------------------



Jammu & Kashmir

22	Kargil A-Type	1372.63	01.03.2013	CPWD	15.08.14	80%	14.08.17	1120.00	252.63	Delay due to J&K problem.
----	------------------	---------	------------	------	----------	-----	----------	---------	--------	---------------------------



23	Miran Sahib(A' Type+ 09 SQ +BW)	2017.63	09.01.2017	CPWD	17.07.17	10%	16.01.19	620.00	1397.63	Work in Progress.
----	---------------------------------	---------	------------	------	----------	-----	----------	--------	---------	-------------------



24	B.S.F. Bandipur ('A-1' Type + 09 SQ + BW)	1606.94	27.07.16	CPWD	30.05.17	5%	29.05.19	420.00	1186.94	Work in progress
----	---	---------	----------	------	----------	----	----------	--------	---------	------------------



25	Kathua ('A' Type+09 SQ+BW)	2097.54	29.09.2014	CPWD	22.07.15	95%	13.10.16	1820.00	277.54	Delay due to J&K Problem. TDC- 06/18
----	----------------------------	---------	------------	------	----------	-----	----------	---------	--------	--------------------------------------



Jharkhand

26	Godda A-1 type+9SQ+BW	1773.64	15.07.2015	CPWD	24.11.15	88%	23.11.16	1620.00	153.64	TDC-30.06.18
----	-----------------------	---------	------------	------	----------	-----	----------	---------	--------	--------------



Karnataka

27	Kodagu (‘A-I’- Type+09 SQ+ BW)	1267.79	20.10.2015	CPWD	01.10.16	73%	17.04.18	1220.00	47.79	Work in Progress . TDC-30.09.18
----	-----------------------------------	---------	------------	------	----------	-----	----------	---------	-------	------------------------------------



28	Chikodi (‘A’- Type+09 SQ+ BW)	1710.97	29.03.2017	CPWD	10.08.2017	18%	10.02.19	620.00	1090.97	Work recently sanctioned.
----	-------------------------------	---------	------------	------	------------	-----	----------	--------	---------	---------------------------



29	Koppal A-Type+09 SQ+BW	1713.94	12.09.2014 23.02.2016	HSCL	10.12.2015 12.03.16	55%	12.06.17 TDC- 30.09.18	1020.00	693.94	Initial delay on account of dispute on land boundaries.
----	---------------------------	---------	--------------------------	------	------------------------	-----	------------------------------	---------	--------	---



30	Karwar (B- Type + B/w)	1944.56	09.01.2015	MES	20.01.15	92%	19.05.17	1920.00	24.56	work in progress
----	---------------------------	---------	------------	-----	----------	-----	----------	---------	-------	------------------



Kerala

31	SAP Trivandrum B-Type+BW	2170.18	22.05.2014	CPWD	23.03.16	73%	15.06.17	1820.00	350.18	Slow progress due to shortage of funds. TDC-30.06.2018.
----	-----------------------------	---------	------------	------	----------	-----	----------	---------	--------	---



32	Kanhagad ('A' Type+ 09 SQ+BW + covering)	2235.49	02.11.2015	CPWD	01.10.16	50%	28.12.17	1020.00	1215.49	Delay due to dispute. TDC-30.09.18
----	---	---------	------------	------	----------	-----	----------	---------	---------	------------------------------------



Madhya Pradesh

33	Chaurai A-Type+9SQ +BW	1284.56	17.06.15	CPWD	25.03.16	36%	24.03.17	620.00	664.56	Slow Progress/Shortage of funds. TDC-30.09.2018
----	------------------------------	---------	----------	------	----------	-----	----------	--------	--------	---



34.	No2 Chindwada ('A' Type+ 09 SQ+BW + covering)	1462.89	21.07.2016	CPWD	01.01.17	19%	31.12.17	620.00	842.89	Work is being started shortly.TDC-31.12.2018.
-----	---	---------	------------	------	----------	-----	----------	--------	--------	---



35.	No-2 Satna ('A'- Type+SQ+BW)	1926.35	07.12.2015 20.12.2016	UPJN	03.01.17	60%	02.01.2019	1020.00	906.35	Work in progress.
-----	------------------------------	---------	--------------------------	------	----------	-----	------------	---------	--------	-------------------



36.	Betul ('A' Type+ 09 SQ+BW + covering)	1647.29	20.07.2016	CPWD	02.12.16	65%	01.02.18	1020.00	627.29	Slow progress/Shortage of funds.
-----	---------------------------------------	---------	------------	------	----------	-----	----------	---------	--------	----------------------------------



37.	No.-2, Rewa Balance work of SB + BW	679.20	29.04.2015	CPWD	25.01.16	98%	24.01.17	675.00	4.20	School building stand completed accepted disputed portion of B/W.
-----	--	--------	------------	------	----------	-----	----------	--------	------	---



38	Dindori ('A' Type+ 09 SQ+BW + covering)	1604.72	21.07.2016	CPWD	01.01.2017	65%	31.12.2017	1020.00	584.72	Work Started. TDC-30.6.18
----	---	---------	------------	------	------------	-----	------------	---------	--------	---------------------------



39.	Datia ('B' Type+ 09 SQ+BW + covering)	1934.54	21.07.2016	CPWD	27.12.16	83%	26.03.18	1420.00	514.54	Work Started.
-----	---------------------------------------	---------	------------	------	----------	-----	----------	---------	--------	---------------



40.	Tikamgarh ('A' Type+ 09 SQ+BW + covering)	1390.21	20.07.2016	CPWD	01.01.2017	85%	26.12.2017	1020.00	370.21	Work started.
-----	---	---------	------------	------	------------	-----	------------	---------	--------	---------------



41.	Sheopur ('A'- Type+BW)	1247.00	08.11.2012	CPWD	28.12.14	98%	28.12.15	1040.00	207.00	Delay on account of slow progress & shortage of funds. TDC-June 2017
-----	------------------------	---------	------------	------	----------	-----	----------	---------	--------	--



Maharashtra

42.	Nanded ('A'type+ 09 SQ+ BW)	2276.52	19.05.2016 08.09.2016	UPJN	15.09.16	73%	14.09.18	1820.00	456.52	Work in Progress.
-----	-----------------------------	---------	--------------------------	------	----------	-----	----------	---------	--------	-------------------



43.	BSF, Chakur('A' Type+ 09 SQ+ BW)	1794.90	01.03.17	UPJN	21.03.2017	35%	20.03.2019	1220.00	574.90	Work in Progress
-----	----------------------------------	---------	----------	------	------------	-----	------------	---------	--------	------------------



Mizoram

44.	Champai ('A-' Type+ 09 SQ+ BW)	2723.98	18.02.2015	CPWD	10.07.16	48%	01.03.18	2420.00	303.98	N.E. Region Problem.
-----	--------------------------------	---------	------------	------	----------	-----	----------	---------	--------	----------------------



Odisha

45	Nayagarh ('A'- Type, SB +09 SQ+ BW + Covering of Courtyard)	1639.01	28.07.16	CPWD	13.12.16	65%	12.12.17	1020.00	619.01	Work In Progress.
----	---	---------	----------	------	----------	-----	----------	---------	--------	-------------------



46.	No.2 Sambalpur ('A' Type+09 SQ+BW)	1646.17	20-06-2016 28.02.2017	BBJ&JCC	14.04.17	41%	Aug,2018	420.00	1126.17	Work in Progress.
-----	------------------------------------	---------	--------------------------	---------	----------	-----	----------	--------	---------	-------------------



47.	Aska ('A' Type SB+09+ SQ+BW)	1701.86	16.05.17	CPWD	21.08.17	15%	20.01.19	620.00	1081.86	Work in Progress.
-----	------------------------------	---------	----------	------	----------	-----	----------	--------	---------	-------------------



48.	Mahuldiha ('A Type+ 09 SQ)	1605.28	07.04.17	CPWD	25.08.17	30%	24.08.18	820.00	785.28	Work in Progress.
-----	----------------------------	---------	----------	------	----------	-----	----------	--------	--------	-------------------



Puducherry

49.	Mahe ('A-1' Type + BW)	1837.52	02.11.2015	CPWD	27.07.17	25%	21.07.2018	820.00	1017.52	Matter is being resolved by Principal. Work suspended due to intervention of local public.TDC-26.09.2018
-----	------------------------	---------	------------	------	----------	-----	------------	--------	---------	--



Rajasthan

50.	Hanumangarh ('A' Type + 09 SQ + BW)	1605.31	06.10.15 28.06.16	HSCL	23.11.16	69%	23.05.18	820.00	785.31	Work in progress.
-----	-------------------------------------	---------	----------------------	------	----------	-----	----------	--------	--------	-------------------



51.	Jalore ('B' Type + 09 SQ + BW)	2028.68	19.07.2016	UPSCIDCO	27.09.16	40%	31.03.18	1020.00	1008.68	Work in progress. TDC- 31.07.18
-----	--------------------------------	---------	------------	----------	----------	-----	----------	---------	---------	---------------------------------



Telangana

52.	Miryalguda A-Type+09SQ+BW	1525.95	23.02.2016	HSCL	March 2016	59%	09.03.17	1020.00	505.03	Work in progress. Initial delay due to land problem. TDC- 30.09.2018
-----	---------------------------	---------	------------	------	------------	-----	----------	---------	--------	--



Tamil Nadu

53.	Perambalur ('A' Type + 09 SQ + BW+ Courtyard covering)	1874.02	20.07.16	CPWD	Work Awarded on 03.01.17	55%	23.04.18	920.00	954.02	Work in Progress
-----	---	---------	----------	------	--------------------------	-----	----------	--------	--------	------------------



Uttar Pradesh

54.	No-4, Varanasi A-Type+09SQ BW	1369.52	24.11.2014	HACL	25.05.15	B/w work done	10.11.16	220.00	1149.52	Go ahead issued to restart the work
-----	----------------------------------	---------	------------	------	----------	------------------	----------	--------	---------	-------------------------------------



55.	Hardoi B-Type+09SQ BW	1867.46	15.07.15 27.12.15	UPSCID CO	08.01.16	95%	07.07.17	1860.00	7.46	Work in progress. TDC- 30.06.2018
-----	--------------------------	---------	----------------------	--------------	----------	-----	----------	---------	------	--------------------------------------



56.	Shivgarh A-Type+BW	1185.16	10.03.2015	UPJN	20.05.15	99%	31.10.17	1170.00	15.16	Initial delay due to dispute on land. 30.06.18
-----	-----------------------	---------	------------	------	----------	-----	----------	---------	-------	---



Uttarakhand

57.	Rajgarhi (A-I Type + 09 SQ + BW)	2061.69	10.11.2014	CPWD	26.09.15	99%	25.09.17	2020.00	41.69	Work in progress. Delay in release of funds due to shortage.
-----	-------------------------------------	---------	------------	------	----------	-----	----------	---------	-------	--



West Bengal

58.	BSF Gandhinagar B type+BW	2000.00	20.02.2014	CPWD	03.11.15	99%	02.02.17	1920.00	80.00	TDC- 30.06.18
-----	------------------------------	---------	------------	------	----------	-----	----------	---------	-------	---------------



59.	Balurghat A type + 11 SQ + BW	1978.34	26.06.2014	CPWD	23.01.16	80%	22.05.17	1520.00	458.34	Delay in handling over of land TDC-30.06.18
-----	----------------------------------	---------	------------	------	----------	-----	----------	---------	--------	---



Lakhasdweep

60.	Kavarati A-I type+11 SQ+BW	2325.64	02.02.2015	CPWD	12.02.16	65%	04.08.17	1620.00	705.64	Initial slow progress. Now progressing well. TDC-30.06.18
-----	-------------------------------	---------	------------	------	----------	-----	----------	---------	--------	---



WORK YET TO BE STARTED

Sl. No.	Name of Kendriya Vidyalaya	AA & ES (Rs. in lakh)	Date of Sanction	Construction Agency	Date of Start	Physical Progress upto date	Stipulated date of completion	Amount released till 01.09.2016 (Rs. in lakh)	Balance liability (Rs. in lakh)	Remark
Bihar										
1	Bela (A-Type +09SQ+BW)	2001.95	22.11.2016	CPWD	220.00	1781.95	Work recently sanctioned and at tender stage.
2.	Harnaut('A'Type+09SQ+BW)	2015.01	16.05.2017	CPWD	20.00	1995.01	Stop order issued
Delhi										
3	3Sec.-22, Rohini ('B' Type)	746.11	03.10.2007	CPWD	Work yet to start	25.00	721.11	Drawing yet to be approved by local bodies. Permission for demolishing of temporary structure awaited
4.	Shahdara ('A' Type S/B)	1460.12	13.04.2018	CPWD	500.00	960.12	Work recently sanctioned
Gujarat										
	AFS Jamnagar (Replacement of SB)	1559.14	02.05.2018	MES	...	Work yet to start	...	20.00	1539.14	
HARYANA										
5	Budayam (Jind) ('B Type + SB+9SQ)	1943.68	26.04.17	CPWD	06.03.18	Started	29.05.19	720.00	1223.68	Recently Started
Himachal Pradesh										
6.	Saloh ('A' Type + 09 SQ)	1620.95	21.06.2017	BSNL		1620.95	IIT vetting is awaited from BSNL to issue go-ahead.
Karnataka										
7.	Haveri ('A' Type + 09 SQ + BW)	2061.80	01.09.2016	FEDO	0.00	2061.80	Stop order issued

Kerala

8.	Ezhimala ('A' Type + BW)	1991.24	24.04.2015	MES	17.08.2017	7%	17.07.19	220.00	1771.24	Delay on the part of MES.
9.	KPA, Ramavarmapuram ('B' Type+ 09 SQ+BW + covering)	2664.40	20.07.2016	CPWD	20.05.17	12%	13.08.18	320.00	2344.40	30.05.2019
10.	Kaduruthy ('A' Type B+09 SQ +BW+covering)	3020.62	27.12.2016	FEDO	0%	0.00	3020.62	Stop order issued

Madhya Pradesh

11.	Harda (A-Type+9SQ+BW)	1651.25	19.09.2016	FEDO	0%	0.00	1651.25	Stop order issued
12.	Malanjkhana ('A' Type SB +9 SQ+BW)	1831.62	28.06.2017	UPJN	..	0%	...	0.00	1831.62	Stop order issued.

Maharashtra

	AFS Thane (Replacement of SB)	1204.89	02.05.2018	MES	...	Work yet to start	...	20.00	1184.89	
--	-------------------------------	---------	------------	-----	-----	-------------------	-----	-------	---------	--

Mizoram

13.	Lunglai ('A' Type+ 09 SQ + BW)	2385.37	24.11.2014 02.05.2017	MAMCO	20.00	2365.37	Stop order issued.
-----	--------------------------------	---------	--------------------------	-------	-----	------	-----	-------	---------	--------------------

Rajasthan

14.	Devgarh ('A' Type SB+ 09 SQ)	1436.72	16.05.2017	CPWD	20.00	1416.72	Stop Order Issued
15.	Tonk ('A-1' Type SB + 09 SQ)	1011.80	21.06.2017	CPWD	20.00	991.80	Stop order issued

Tamilnadu

16.	AFS, Tanjavur 'A' Type + 09 SQ + BW)	1835.59	02.11.2015	MES	20.00	1815.59	Delay on the part of MES.
-----	--------------------------------------	---------	------------	-----	-----	-----	-----	-------	---------	---------------------------

Telangana

17.	Sirsilla ('A' Type SB+ 09 SQ+ BW)	1651.61	16.03.2017	HSCCL	1651.61	Stop order issued
-----	-----------------------------------	---------	------------	-------	-------	-------	-------	---------	--------------------------

Uttar Pradesh

18.	Deoria ('A' Type + 09 SQ + BW)	1415.74	25.06.2013	CPWD	...	Work yet to start	...	70.00	1345.74	Encroachment on land.
19.	Sharawasti ('A' Type+09 SO+BW)	1585.12	20-06-2016 07.04.2017	BBJ&JCC	...	Just Started	...	20.00	1365.12	Go-ahead issued to restart the work on 26.03.18
20..	Gangarani,Kushinagar (B Type SB + 09 SQ+BW)	1680.66	26.04.17	CPWD	20.00	1660.66	Stop order issued
21.	Siddarthnagar (B Type SB + 09 SQ+BW)	1820.28	16.05.17	CPWD	20.00	1600.28	Works recently sanctioned. Work held up due to HT Line in LOP.

Uttarakhand

22.	Bhimtal (A Type +BW+Covering)	1792.79	21.03.2017	CPWD	20.00	1772.79	Stop order issued
23.	Gopeshwar ('A-1 Type SB+09+ SQ+B/W)	2185.97	26.06.2017	UPJN		2185.97	Stop order issued

West Bengal

24.	Kalimpong ('A-1'+ BW)	1430.74	10.12.2014	MES	...	9%	...	420.00	1010.74	Slow Progress.
-----	-----------------------	---------	------------	-----	-----	----	-----	--------	---------	-----------------------
